

PROJECT KICKOFF DOCUMENT

Zion Energy Services
Dispatch & Workforce Operations Platform

Document Version	Project Kickoff
Date	February 2026
Prepared By	Aaditya Kapoor and Team
Organization	Nile Technologies Pvt. Ltd.
Client	Zion Energy Services
Reference Proposal	Techno-Commercial Proposal V4.0
Classification	Confidential

Submitted and Presented by Nile Technologies Pvt. Ltd.

1. Executive Overview

This document serves as the official kickoff reference for the Zion Energy Services Dispatch and Workforce Operations Platform, a purpose-built, proprietary software solution developed by Nile Technologies Pvt. Ltd. It establishes a shared understanding of what is being built, how it will be delivered, the technical architecture underpinning it, and the responsibilities of all parties involved.

This is the first formal deliverable of the engagement and satisfies the requirements of Payment Milestone 1: Project Kickoff, Architecture Finalized, and Delivery Plan Approved.

1.1 What We Are Building

Zion Energy Services operates in a highly dynamic, field-driven environment where teams, equipment, and job sites are constantly moving. The platform being built addresses a core operational need: replacing fragmented tools, manual tracking, and reactive decision-making with a unified, intelligent system.

The solution comprises two interconnected components:

- An Admin Web Dashboard, giving operations, dispatch, payroll, and management teams a real-time command view of the entire field workforce.
- An Employee Mobile App, giving field employees a simple, reliable interface to execute their work compliantly: logging client information, checking in and out of jobs, and tracking mileage.

1.2 Core Business Outcomes

The platform is designed to deliver the following measurable outcomes for Zion:

Operational Visibility	Real-time map view of all employees, job sites, and active assignments, no more manual check-ins by phone.
Compliance & SLA Tracking	Automated detection of late arrivals, geo-fence violations, and SLA breaches, before they become problems.
Overtime Cost Control	Predictive OT monitoring at employee, team, and org level with cost impact visibility before thresholds are breached.
Payroll Accuracy	Verified hours from geo-tagged check-ins feed directly into payroll, eliminating manual reconciliation.
Mileage Billing	Automatic trip detection and work/personal classification enables accurate client billing and tax rebate processing.
Client Documentation	Field employees capture notes, map drawings, and documents on-site; all stored centrally under each client profile.

2. Technical Architecture

The platform is built on a modern, scalable, cloud-ready architecture. The design ensures the system can support Zion's current operational scale while remaining extensible for future integrations and intelligence layers.

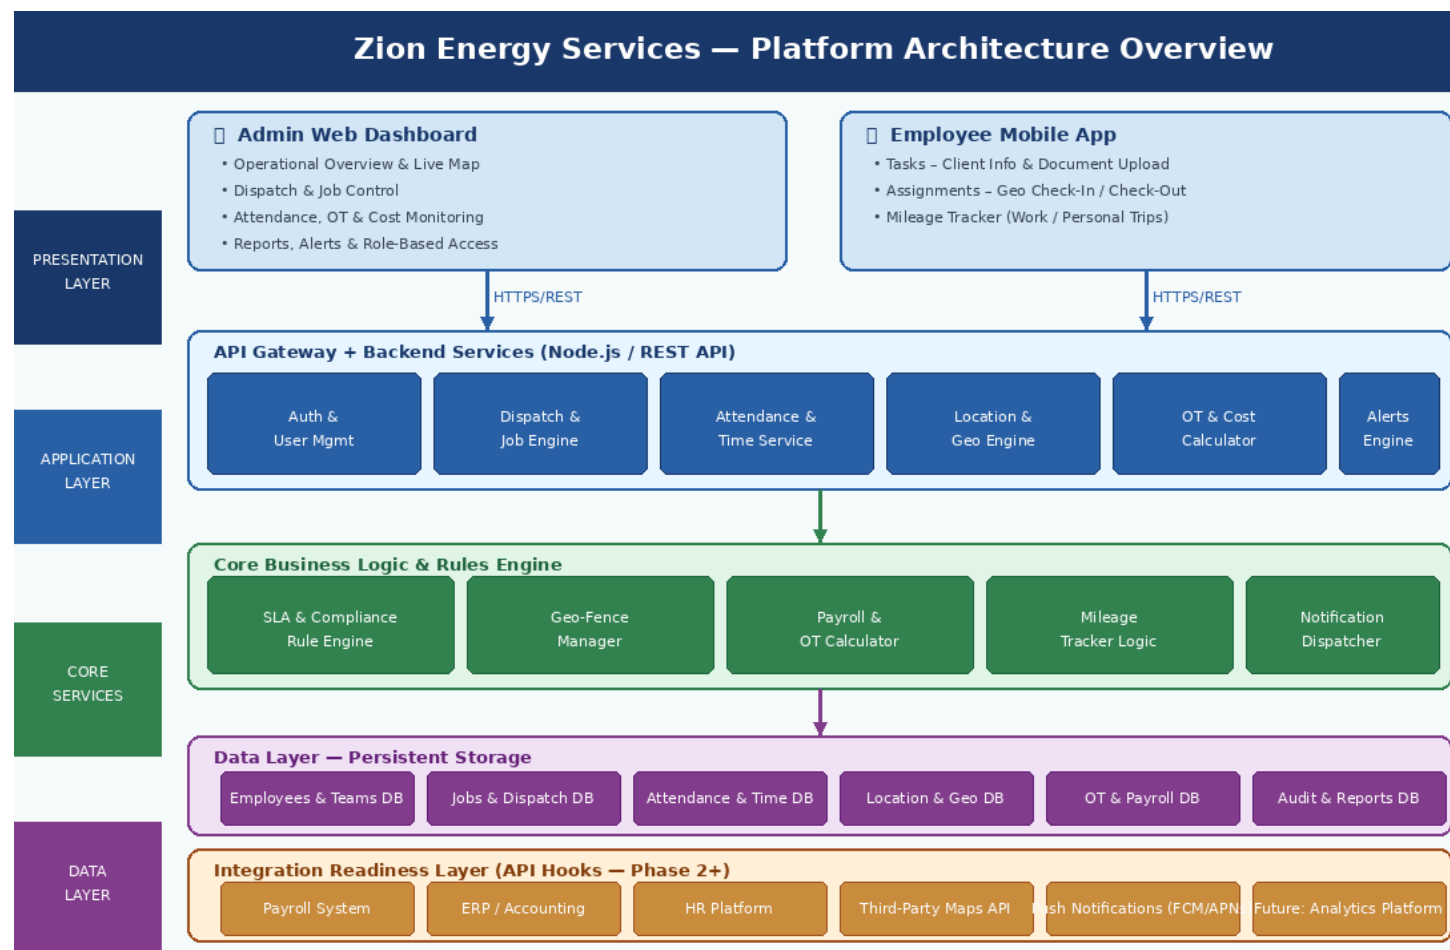


Figure: Platform Architecture, Layered Overview

2.1 Architecture Layers

Presentation Layer

The user-facing layer comprises two applications built for distinct user types and contexts:

- **Admin Web Dashboard,** A responsive web application for operations managers, dispatchers, and payroll teams. Built for desktop use with full feature access.
- **Employee Mobile App,** A native mobile application (iOS and Android) built for simplicity and reliability under real field conditions, including remote locations and intermittent connectivity.

Application Layer, API Gateway & Backend Services

All business logic resides in a structured backend built on a RESTful API architecture. Key service domains include Authentication, Dispatch Engine, Attendance Service, Location & Geo Engine, Overtime Calculator, and Alerts Engine. All communication between the front-end and backend is over HTTPS.

Core Services & Rules Engine

A dedicated rules layer handles configurable business logic, SLA thresholds, geo-fence definitions, OT rules, mileage classification logic, and notification triggers. These are centrally configurable by the admin without requiring code changes.

Data Layer

Persistent storage is organized by domain: Employees & Teams, Jobs & Dispatch, Attendance & Time, Location & Geo, OT & Payroll, and Audit & Reports. All data originates from a single system, ensuring consistency across reporting and operations.

2.2 Technology Stack

Frontend, Web	Web Dashboard
Frontend, Mobile	React Native (iOS & Android), Single codebase, native performance
Backend / API	RESTful API Gateway
Database	MYSQL
Location Services	Google Maps / Mapbox SDK / Alternative, Geo-fencing
Push Notifications	Firebase Cloud Messaging (FCM) + Apple Push Notification Service (APNs)
Authentication	JWT-based authentication + role-based access control (RBAC)
Hosting	Cloud-hosted (AWS), setup and deployment included
Mobile Distribution	Apple App Store + Google Play Store, submission included
IP & Source Code	100% transferred to Zion upon project completion

3. Operational Workflow

The platform is designed around how work actually happens in the field, not just how it is reported afterward. The end-to-end workflow follows a logical sequence from initial setup through to reporting and payroll.

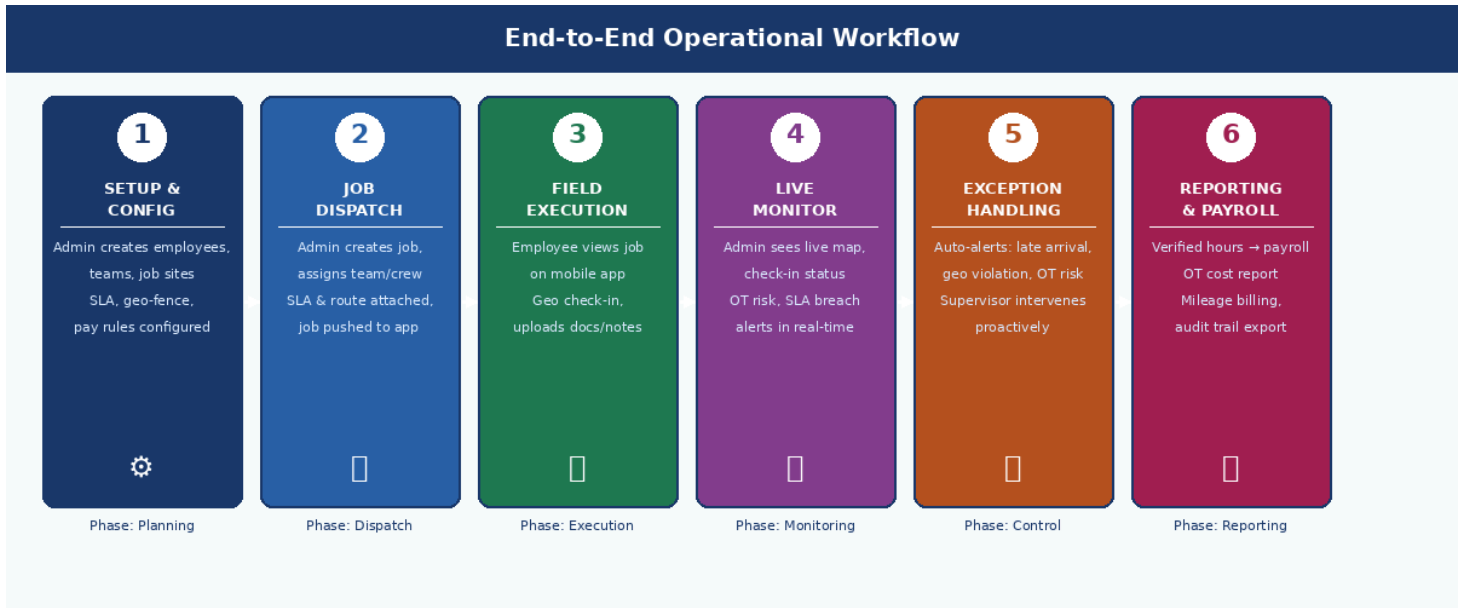


Figure: End-to-End Operational Workflow, 6 Phases

3.1 Workflow Phase Descriptions

#	Phase	What Happens
1	Planning & Setup	Admin configures employees, teams, roles, job sites, pay rules, SLA thresholds, geo-fences, and business rules. Client information master is populated. This is the foundation layer, everything downstream depends on clean setup data.
2	Job Dispatch	Admin creates jobs and assigns them to teams or individuals. Each job carries its SLA configuration, geo-fence, route, time window, and any client documents. Jobs are instantly pushed to the assigned employee's mobile app.
3	Execution in the Field	The employee sees the assigned job on their app, navigates to the site, and completes a geo-tagged check-in. They can log notes, upload documents, and drop location pins. Any rule violations (geo-fence breach, early departure) are flagged in real time.
4	Live Monitoring	Operations teams monitor workforce activity through the Admin Dashboard's live map view. Overtime risk, attendance status, job progress, and compliance indicators are all visible in real time without manual chasing.
5	Exception Handling	The platform surfaces anomalies automatically, late arrivals, geo-fence violations, overtime risks, or unusual patterns, with confidence indicators. Supervisors are alerted proactively and can intervene before issues escalate.
6	Reporting & Payroll	Verified hours from geo-tagged check-ins flow directly into timesheet and payroll reports. Mileage data is processed for client billing or tax rebates. All reports are exportable for audits, management review, and compliance.

4. Employee Mobile App, Three Core Workflows

The Employee Mobile App is the field-facing side of the system. It is intentionally simple, fast, and reliable, designed for real field conditions including remote locations and inconsistent connectivity. The app contains three distinct modules, each serving a different operational purpose.

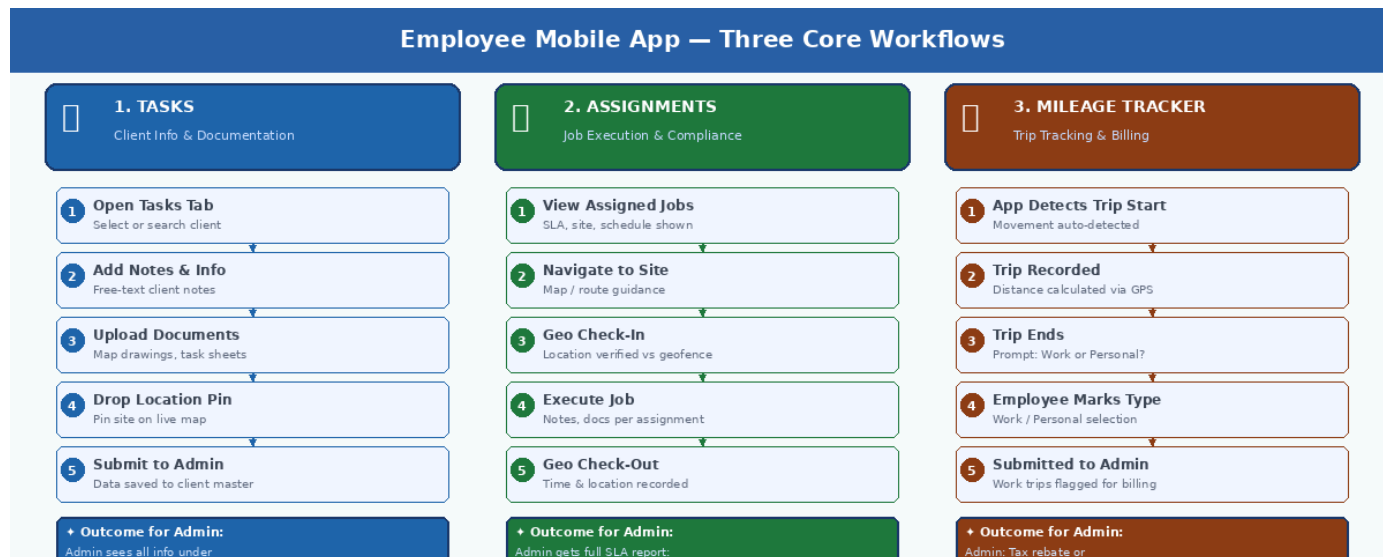


Figure: Employee Mobile App, Three Workflow Modules

4.1 Module 1, Tasks (Client Information & Documentation)

This module enables field employees to proactively build out the client information master, without needing to be assigned a formal job.

- The employee opens the Tasks tab and selects or searches for a client.
- They can add free-text notes covering any client-specific information gathered in the field.
- They can upload documents, map drawings, task sheets, site layouts, client instructions, directly from their phone.
- They can drop a live location pin at their current position, tagging it to the client record.
- All submissions are compiled under that client's profile in the Admin Console, ready for use during job assignment and dispatch.

Admin Value: Before a job is even created, admin has rich, field-gathered intelligence about each client site, drawings, notes, coordinates, all in one place.

4.2 Module 2, Assignments (Job Execution & Geo-Compliance)

This is the core operational module where formal assigned jobs are executed.

- The employee sees all jobs assigned to them, with the schedule, client site, SLA details, and any pre-attached documents.
- On arrival, they perform a geo-tagged check-in. The system verifies they are within the configured geo-fence for that job site.
- If they check in from outside the geo-fence, or check out unexpectedly, the system flags this as a violation and alerts the admin.
- Throughout the job, the employee can log notes and upload job-specific documents.
- On completion, they check out. Their time on-site is recorded and tied to that specific job and assignment.

Admin Value: Automated SLA reporting, late check-ins, early departures, geo-violations, total hours per job, all without any manual tracking.

4.3 Module 3, Mileage Tracker

This module automatically tracks employee trips and classifies them for billing or tax purposes.

- The app detects when the employee starts moving (above a defined speed threshold).
- GPS calculates the trip distance in real time.
- When the trip ends, the app prompts the employee: "Was this a Work Trip or Personal Trip?"
- Work trips are automatically reported to the Admin Dashboard under that employee's daily operations record.
- Admin can then designate work mileage for client billing or for company tax rebate processing.

Admin Value: Accurate, automated mileage records replace manual logbooks. Work trips are billable. All data is exportable for finance.

5. Admin Dashboard, Key Screens

The Admin Web Dashboard acts as the operational command centre for Zion's management and dispatch teams. Below is the conceptual layout of the primary operational screen.

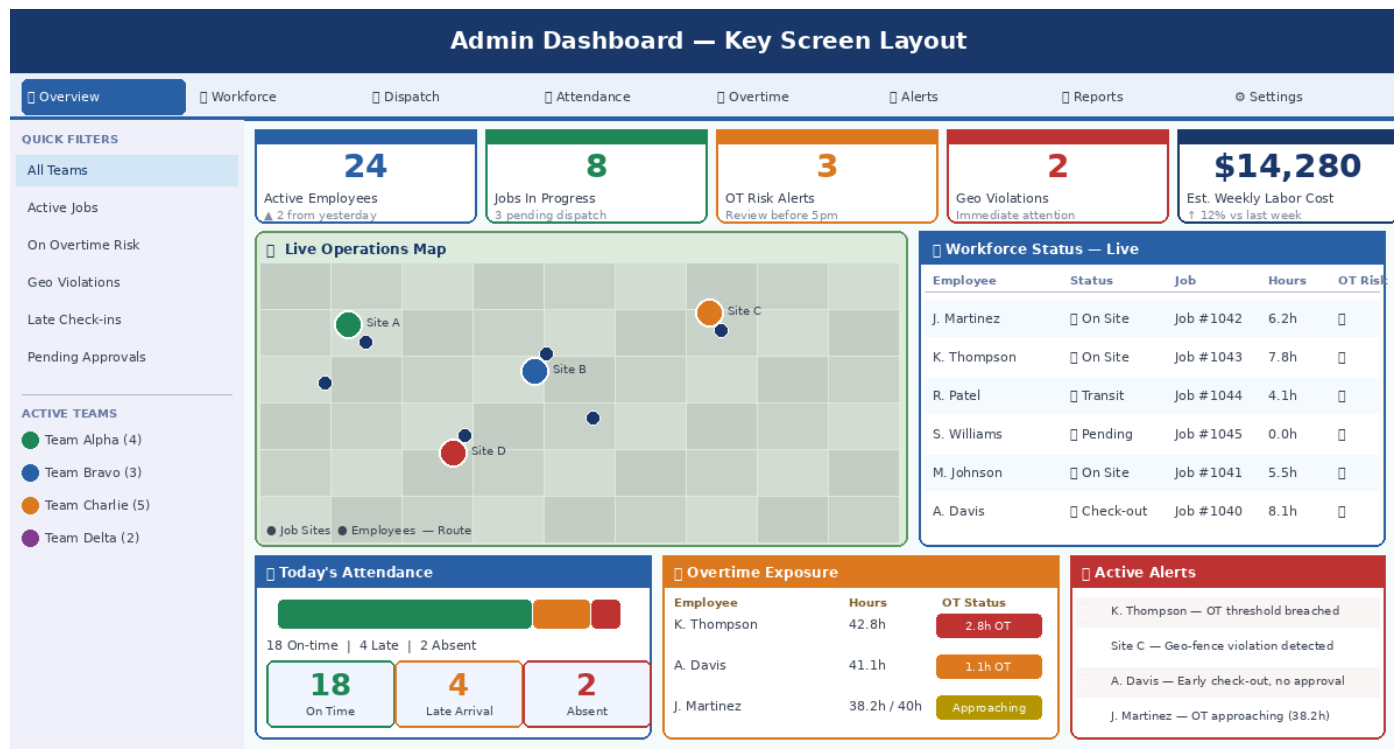


Figure: Admin Dashboard, Operational Overview Screen Layout

5.1 Dashboard Module Summary

Module / Block	Key Functionalities	Priority
Operational Overview	Live workforce status, active team count, attendance summary, OT exposure, interactive map with employee and job site positions, route overlays	Critical
Employee & Team Management	Centralised employee directory, team composition, role assignments, supervisor mapping, compliance posture per employee	Critical
Dispatch & Job Control	Create and assign jobs, attach SLA/geo-fence/route/documents, monitor job progress and execution status in real time	Critical
Attendance & Time Tracking	Daily attendance overview, geo-tagged check-in/out records, late arrivals, early exits, absences flagged with contextual data	Critical
Overtime & Cost Monitoring	Real-time and predictive OT exposure by employee and team, projected cost impact, configurable threshold rules	Critical

Module / Block	Key Functionalities	Priority
Alerts & Exceptions	Automated alerts for geo-fence breaches, SLA violations, OT risks, unusual patterns, with confidence indicators and priority ranking	High
Mileage Reporting	Daily work trip reports per employee, total work mileage, one-click export for billing or tax rebate processing	High
Reporting & Analytics	Exportable payroll reports (hours × pay rate), OT reports, compliance summaries, audit trails, job execution logs	High
SLA Configuration	Per-client SLA rules, permitted waiting time, missed attendance triggers, breach escalation logic, configurable without code changes	High
Role-Based Access Control	Granular access levels: Super Admin, Operations Manager, Dispatcher, Payroll, Read-Only. Each role sees only what they need.	High

7. Delivery Timeline Plan

Phase 1 spans 16 weeks from project kickoff. The timeline is structured into three sub-phases aligned with the payment milestones agreed in the Techno-Commercial Proposal V4.0.

7.1 Timeline Summary

Sub-Step 1	Weeks 1–4, Design & Alignment: Requirements confirmation, technical architecture sign-off, UI/UX design for web and mobile
Sub-Step 2	Weeks 5–14, Core Development & Iterations: All 9 delivery blocks developed, integrated, and tested in iterative sprints
Sub-Step 3	Weeks 15–16, Stabilization & Launch Readiness: QA completion, UAT, bug fixes, production deployment, App Store submission
Post-Launch	Weeks 17–20, Complimentary 4-Month Support: Bug fixes, minor enhancements, and operational support at no additional cost

9. Roles, Responsibilities & RACI

The following RACI matrix defines accountability across all key project activities. Clear ownership prevents ambiguity and ensures the project moves efficiently.

Activity	Aaditya(Nile)	DevTeam	PM(Nile)	Hunter(Zion)	Legend
Requirements & Scope Confirmation	A	R	C	R	R = Responsible
Technical Architecture Design	C	R	A	I	A = Accountable
UI/UX Design & Wireframes	C	R	A	R	C = Consulted
Mobile App Development	I	R	A	C	I = Informed
Web Dashboard Development	I	R	A	C	
SLA & Geo-Fence Configuration	C	I	A	R	
QA Testing & Bug Reporting	C	R	A	C	
User Acceptance Testing (UAT)	C	I	A	R	
App Store Submission	I	R	A	C	
Production Deployment	C	R	A	I	
Post-Launch Support	A	R	C	I	
Change Request Approvals	A	I	C	R	

9.1 Key Contacts

Aaditya Kapoor, Nile	Primary commercial and strategic contact. Escalation point for scope, contracts, and delivery.
Payal Chhikara, Nile	Program Manager. Key Figure in Delivery Milestone Presentations and subsequent project planning and execution (Technical Side)
Project Manager, Nile	Day-to-day delivery lead. Sprint planning, dev coordination, milestone tracking, and client communication during build.
Hunter, Zion	Primary client stakeholder. Business requirements owner, UAT lead, and sign-off authority for milestones.

12. Immediate Next Steps

Following this kickoff meeting, the following actions will be initiated immediately:

Nile Technologies, Immediate Actions

1. Set up project communication channel (Slack / WhatsApp / Email) with agreed response SLAs.
2. Assign dedicated Project Manager and share contact details with Zion team.
3. Begin technical architecture documentation and prepare for formal sign-off. (Architecture Plan)
4. Initiate UI/UX design process, web dashboard wireframes first, then mobile app.
5. Set up development environment, repository.
6. Prepare detailed sprint plan for Weeks 5–14 and share with Zion for visibility. (Delivery Plan)

Zion Energy Services, Immediate Actions

7. Confirm primary point of contact for day-to-day project communication.
8. Create Web domain, Apple Developer Account and Google Play Console account (retain platform ownership). - Low to Medium Priority at Kickoff
9. Sign off on this Kickoff Document

12.1 Communication & Governance

Project Updates	Status update shared by Nile PM at pre-established communication channels or Online Meetings as per client's convenience
Sprint Demos	Demo sessions where completed features are demonstrated for review and feedback
Escalation Path	Aaditya Kapoor (Nile) ↔ Hunter (Zion), direct line for any commercial or strategic matters
UAT Process	Zion team tests against defined acceptance criteria.
